ID	Task Name	Duration	Start	Finish
1	**PRE-CONSTRUCTION PROCESS**	**561 days**	**Fri 2/1/08**	**Fri 4/16/10**
2				
3	**PROJECT KICK-OFF**	**48 days**	**Fri 2/1/08**	**Tue 4/8/08**
8				
9	**CITY OF PHOENIX DSD SITE PLAN APPROVAL PROCESS**	**299 days**	**Tue 4/8/08**	**Fri 6/12/09**
10	Pre Pre-Application Meeting / Submit Prelim Site Plan Package	0 days	Tue 4/8/08	Tue 4/8/08
11	City Assigns Site Plan Review Meeting	15 days	Wed 4/9/08	Tue 4/29/08
12	Pre Pre-App Site Plan Review Meeting	0 days	Tue 4/29/08	Tue 4/29/08
13	Settle Variance / Special Permit Issues	208 days	Wed 4/30/08	Wed 2/25/09
14	Pre-App Meeting (For REVISED Scope)	0 days	Thu 2/26/09	Thu 2/26/09
15	City Assigns 'Post-App' Meeting	5 days	Fri 2/27/09	Thu 3/5/09
16	'Post-App' Meeting	0 days	Thu 3/5/09	Thu 3/5/09
17	City Grants Approval to Submit Preliminary Site Plan	12 days	Thu 4/2/09	Fri 4/17/09
18	Submit Preliminary Site Plan	0 days	Fri 4/17/09	Fri 4/17/09
19	City Reviews Preliminary Site Plan	19 days	Mon 4/20/09	Thu 5/14/09
20	Site Plan Review Meeting w/ City	0 days	Thu 5/14/09	Thu 5/14/09
21	Incorporate City Comments	3 days	Fri 5/15/09	Tue 5/19/09
22	ZA Variance (12' Wall)	0 days	Thu 5/21/09	Thu 5/21/09
23	Variance Approved (Appeal Duration)	15 days	Fri 5/22/09	Fri 6/12/09
24	Approved to Submit CD's	0 days	Fri 6/12/09	Fri 6/12/09
25				
26				
27	**SELECT DESIGN CONSULTANTS**	**60 days**	**Fri 2/1/08**	**Thu 4/24/08**
31				
32	**DESIGN & ENGINEERING PROCESS**	**377 days**	**Thu 3/13/08**	**Fri 9/4/09**
33	Native Plant Salvage Inventory Plan	8 days	Thu 3/13/08	Mon 3/24/08
34	Civil - Grading & Drainage Drawings	10 days	Fri 2/27/09	Thu 3/12/09
35	Building (Arch) / Construction Documents	10 days	Fri 2/27/09	Thu 3/12/09
36	Revise Civil Grading & Drainage Drawings	***12 days***	Mon 7/6/09	Tue 7/21/09

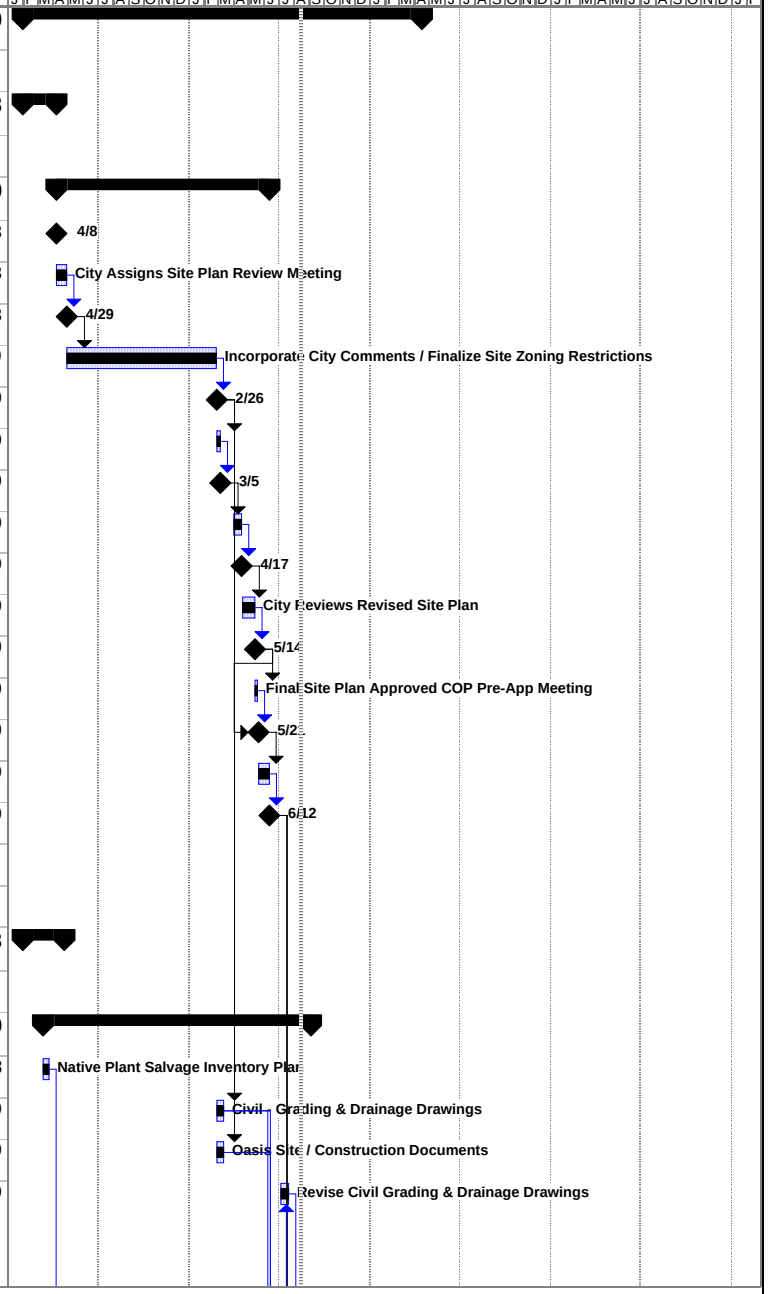

Brophy College Preparatory
Thu 8/13/09

Task	Summary	Rolled Up Progress	Group By Summary		
Critical Task	Rolled Up Task	Split	Deadline		
Progress	Rolled Up Critical Task	External Tasks			
Milestone	Rolled Up Milestone	Project Summary			

ID	Task Name	Duration	Start	Finish
37	Revise Building (Arch) / Construction Drawings (phase 1)	*7 days*	Thu 7/16/09	Fri 7/24/09
38	Revise Building (Arch) / Construction Drawings (phase 2)	*10 days*	Mon 8/24/09	Fri 9/4/09
39				
40	**CITY APPROVAL PROCESS**	**384 days**	**Tue 3/25/08**	**Mon 9/28/09**
41	COP Review Native Plant Salvage/Inventory - 1st Review	12 days	Tue 3/25/08	Wed 4/9/08
42	COP Review Civil - Grading & Drainage Drawings - 1st Review	17 days	Wed 6/10/09	Thu 7/2/09
43	COP Review Building Drawings - 1st Review (phase 1)	22 days	Mon 6/15/09	Wed 7/15/09
44	COP Review Building Drawings - 1st Review (phase 2)	*49 days*	Mon 6/15/09	Fri 8/21/09
45	COP Review Civil - Grading & Drainage Drawings - 2nd Review	17 days	Wed 7/22/09	Thu 8/13/09
46	COP Review Building Drawings - 2nd Review (phase 1)	*20 days*	Mon 7/27/09	Fri 8/21/09
47	COP Review Building Drawings - 1st Review (phase 2)	*15 days*	Tue 9/8/09	Mon 9/28/09
48				
49	**PERMITS**	**372 days**	**Wed 4/9/08**	**Mon 9/28/09**
50	Native Plant Salvage (bid, box, salvage) -Oasis Demo	0 days	Wed 4/9/08	Wed 4/9/08
51	Receive At-Risk G/D Permit	0 days	Thu 8/13/09	Thu 8/13/09
52	**Receive Grading & Drainage Permit**	0 days	Thu 8/20/09	**Thu 8/20/09**
53	**Receive Building Permit**	0 days	Mon 9/28/09	**Mon 9/28/09**
54				
55	**CONSTRUCTION**	**199 days**	**Tue 7/7/09**	**Fri 4/16/10**
56	Demo (Drywells, Xavier wall, and Palm Trees @ Highland)	10 days	Tue 7/7/09	Mon 7/20/09
57	**Phase I: Site & Practice Fields (Turf)**	50 days	Fri 8/14/09	Fri 10/23/09
58	Grass Grow-In Period	15 days	Mon 10/19/09	Fri 11/6/09
59	Useable Grass Pracitce Fields	0 days	Fri 11/6/09	Fri 11/6/09
60				
61	**Phase II: Main Field, Buildings F, G Construction**	140 days	Tue 9/29/09	Fri 4/16/10
62	Substantial Completion	0 days	Fri 4/16/10	Fri 4/16/10

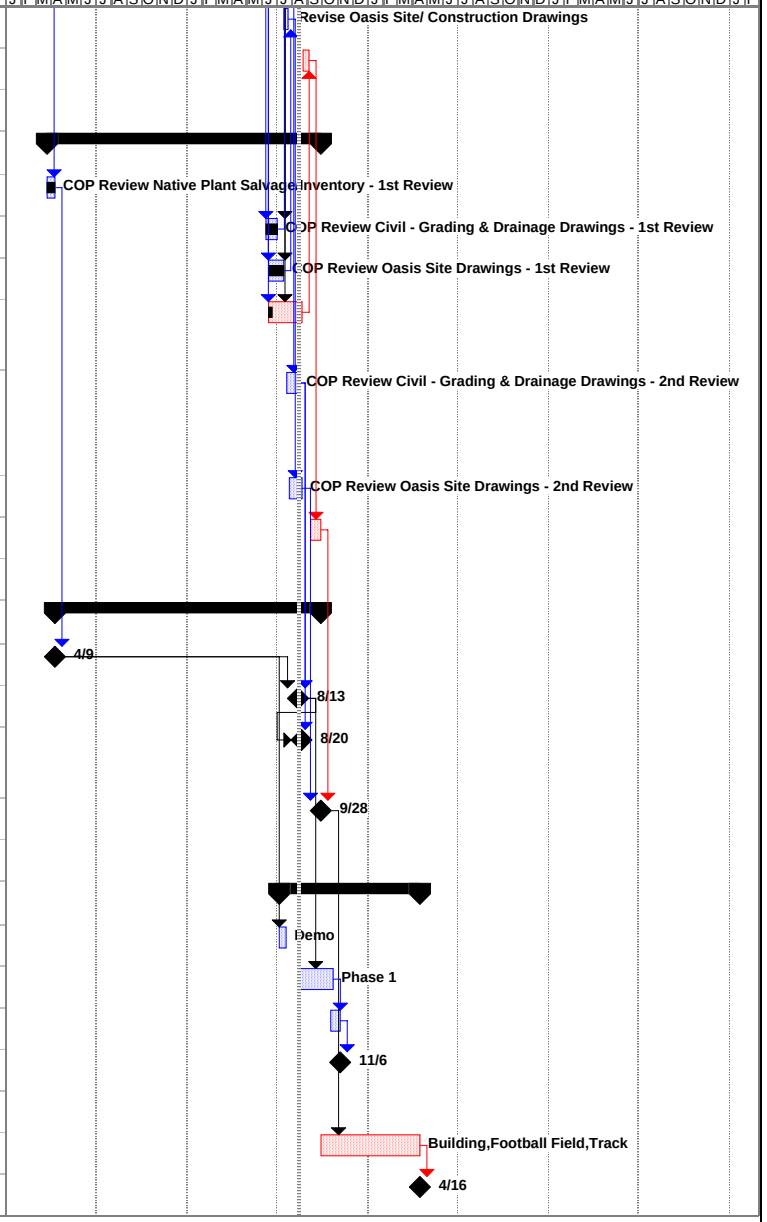

Brophy College Preparatory
Thu 8/13/09

Task	Summary	Rolled Up Progress	Group By Summary		
Critical Task	Rolled Up Task	Split	Deadline		
Progress	Rolled Up Critical Task	External Tasks			
Milestone	Rolled Up Milestone	Project Summary			
